



WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

DESCRIPTION

Roadway Improvements

TYPE

Monday, October 3, 2022

FROM DATE

Sunday, October 9, 2022

TO DATE

568- 574

OF

855

PROJECT CONTRACT DAYS REPRESENTED

JTA P-20-013

FPID NO.

Duval

COUNTY

P-16-037

CONTRACT NO.

2109-15

TASK WORK ORDER NO.

574 OF 855

PROJECT TOTAL

0/7

THIS WEEK / GRAND TOTAL
NON-PURSUIT DAYS

0/7

THIS WEEK / GRAND TOTAL
NON-CONFORMANCE DAYS

0 / 7

THIS WEEK / GRAND TOTAL
WEATHER DAYS GRANTED

Ted Rice

PROJECT ADMINISTRATOR

Scott Ferreira / Eisman & Russo

LEAD/SENIOR INSPECTOR

GENERAL REMARKS - PRIME CONTRACTOR

Watson Civil Construction

Monday, October 3, 2022

CD 568 of 855

FDOT Right of way

Center median existing base operations

Station 19+00 to Station 22+60

- Continue demo and grading after Tropical Storm Ian.
- Survey crew to re-shoot area after grading operations to mark final grade

JTA Right of way

Destry crew

WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

Roadway Improvements

DESCRIPTION

TYPE

Assisted with final 2 loads of sheet-pile.

- Last two loads of sheet pile rescheduled for tomorrow.
- Review M.O.T. and Erosion control.
- Identified 7 area where silt fence needed to be repaired/replaced. Contractor reviewed and made repairs on this day.

Brown Brothers LLC

Station 84+20RT to Station 85+22RT of CL

- Subcontractor scheduled to pour curb and sidewalk from 32lf RT of CL to 69lf RT of CL of construction
- Subcontractor rescheduled pour due to mechanical issues with equipment and vehicle.

Watson Civil Construction

Tuesday, October 4, 2022

CD 569 of 855

FDOT Right of way

Center median existing base operations

Station 18+47 to Station 22+60

- Continue demo and grading after Tropical Storm Ian.
 - Survey crew to re-shoot area after grading operations to mark final grade.
- Note:**
- 6in of lime rock, in lieu of subgrade, will be installed as well as OBG 9 10in of base in 4in and 6in lifts.
 - New Pit Proctor as of October 1st. Lime rock 26098 stockpiles will fall under the new Quarter as 26098 LIMEROCK INDUSTRIES, INC. B01 1 lime rock Base, moisture 12.3 and pcf of 117

JTA Right of way

Brown Brothers LLC

WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

Roadway Improvements

DESCRIPTION

TYPE

Station 84+20RT to Station 85+22RT of CL Ashgrove at Alta Drive

- Subcontractor scheduled to pour curb and sidewalk from 32lf RT of CL to 69lf RT of CL of construction
- QC and VT shall verify embankment tests are completed prior to concrete placement.

Deliveries:

- Limerock delivery to laydown yard today. Sample will be BP006Q and BP006V (4 bags each) for LBR testing.

Notes:

- Alta Drive at Deceleration ramp from NB I295: A-Frame Yield sign to be reinstalled to ensure sign distance visibility for traveling public.
- Alta Drive at Deceleration ramp from NB I295: Post mounted "DO NOT ENTER" sign needs to be reinstalled.
- Alta Drive at Daylilly Road: Post mounted Stop sign to be reinstalled.

Watson Civil Construction

Wednesday, October 5, 2022

CD 570 of 855

FDOT Right of way

Center median existing base operations

Station 18+47 to Station 22+60

- Continue demo and grading after Tropical Storm Ian.
- Survey crew to re-shoot area after grading operations to mark final grade.
- 6in of lime rock in lieu of subgrade placed by contractor. Lot compacted and tested, with passing results, by both QC and VT.
- Lime rock used is from last quarter, Stockpile A, at Alta Drive and Alta Lakes. Contractor understands that rock must pass new quarter pit proctor for 26098.

Note:

WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

Roadway Improvements

DESCRIPTION

TYPE

- 6in of lime rock, in lieu of subgrade, will be installed as well as OBG 9 10in of base in 4in and 6in lifts.
- New Pit Proctor as of October 1st. Lime rock 26098 stockpiles will fall under the new Quarter as 26098 LIMEROCK INDUSTRIES, INC. B01 1 lime rock Base, moisture 12.3 and pcf of 117

JTA Right of way

Brown Brothers LLC

Station 84+20RT to Station 85+22RT of CL Ashgrove at Alta Drive

- Subcontractor poured curb and sidewalk from 32lf RT of CL to 69lf RT of CL of construction
- QC and VT verified embankment tests and completed them prior to concrete placement.

Deliveries:

- Limerock delivery to laydown yard today. Sample as BP006Q and BP006V (4 bags each) for LBR testing.
- Both QC and VT sampled new limerock as BP006IV. Samples taken and delivered to labs for LBR testing on this date.

Notes:

- Alta Drive at Deceleration ramp from NB I295: A-Frame Yield sign to be reinstalled to ensure sign distance visibility for traveling public. Sign installed on this day.
- Alta Drive at Deceleration ramp from NB I295: Post mounted "DO NOT ENTER" sign needs to be reinstalled. Sign involved in accident, Jorgenson scheduled to repair/replace.
- Alta Drive at Day Lily Road: Post mounted Stop sign to be reinstalled. Sign repaired by T.C.P.

Watson Civil Construction

Thursday, October 6, 2022

CD 571 of 855

WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

Roadway Improvements

DESCRIPTION

TYPE

FDOT Right of way

Center median existing base operations

Station 18+47 to Station 22+60

- Continue demo and grading after Tropical Storm Ian.
- Survey crew to re-shoot area after grading operations to mark final grade.

Note:

- 6in of lime rock, in lieu of subgrade, will be installed as well as OBG 9 10in of base in 4in and 6in lifts.
- New Pit Proctor as of October 1st. Lime rock 26098 stockpiles will fall under the new Quarter as 26098 LIMEROCK INDUSTRIES, INC. B01 1 lime rock Base, moisture 12.3 and pcf of 117

JTA Right of way

Destry crew:

Cleanup and mow JTA right of way

Deliveries:

- Lime rock delivery to laydown yard today. 15 loads, 400tons+/-

Watson Civil Construction

Friday, October 7, 2022

CD 572 of 855

FDOT Right of way

Center median existing base operations

Station 18+47 to Station 22+60

- Continue demo and grading after Tropical Storm Ian.
- Survey crew to re-shoot area after grading operations to mark final grade.



WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

Roadway Improvements

DESCRIPTION

TYPE

Note:

- 6in of lime rock, OBG 9 10in of base in 4in and 6in lifts.
- New Pit Proctor as of October 1st. Lime rock 26098 stockpiles will fall under the new Quarter as 26098 LIMEROCK INDUSTRIES, INC. B01 1 lime rock Base, moisture 12.3 and pcf of 117
- QC and VT tested both lifts as separate lots.

JTA Right of way

Destry crew:

Cleanup and mow JTA right of way

Deliveries:

- **None**

Saturday 10-08-2022 / CD 573 of 855

- No scheduled operations

Sunday 10-09-2022 / CD 574 of 855

- No scheduled operations

GENERAL NOTES

Erosion control discrepancies given to contractor on 9-22-22. Corrected 9-23-22 along Rt of CL.

WEEKLY PROGRESS REPORT

JACKSONVILLE TRANSPORTATION AUTHORITY

JTA ALTA DR. IMPROVEMENTS / FDOT I-295 @ Alta Dr.

Roadway Improvements

DESCRIPTION

TYPE

MOT and SWPPP reviewed. Correction completed by contractor

- **CONTROLLING ITEMS OF WORK**

- [A4120] Earthwork Phase 2A - Zone 2
- [A4150] Curb & Gutter Phase 2A - Zone 2
- [A3780] Lighting Directional Bore - STA 84+60 Phase 2A - Zone 2
- [A3790] Lighting Directional Bore - STA 88+60 Phase 2A - Zone 2
- [A6250] Earthwork Phase 1 A2 - Zone 1
- [A6940] Asphalt Paving Phase 1 A2 - Zone 1

-

ACCIDENTS

- NONE

DEFICIENCY LETTERS

- None

VISITORS

- Heart Electric, JEA, CSX, J&K underground

WEATHER

- None

PROGRESS PLANNED FOR NEXT WEEK

Work planned for next two weeks -

Controlling Items of Work and 3 Week Look Ahead to be submitted bi-weekly - (By COB on Tuesday prior to Progress Meetings)

- Curb/Sidewalk Installation- Various Locations
- Subgrade and Base, PH 2A2 and PH 1 C1
- WM Remove existing- PH 2A2
- Install Drainage, PH 2A2
- Sheet Pile Installation - PH 4B
- Light Pole Installation - PH 2A2
- Traffic Shift - PH 1 C1
- Directional-Boring - PH 2A2

PHOTOGRAPHS



Sta 18+47 to 22+80 Demo median




Sta 18+47 to 22+80 Demo median

Eisman & Russo, Inc



Sta 18+47 to 22+80 Demo median


Sta 18+47 to 22+80 Demo median

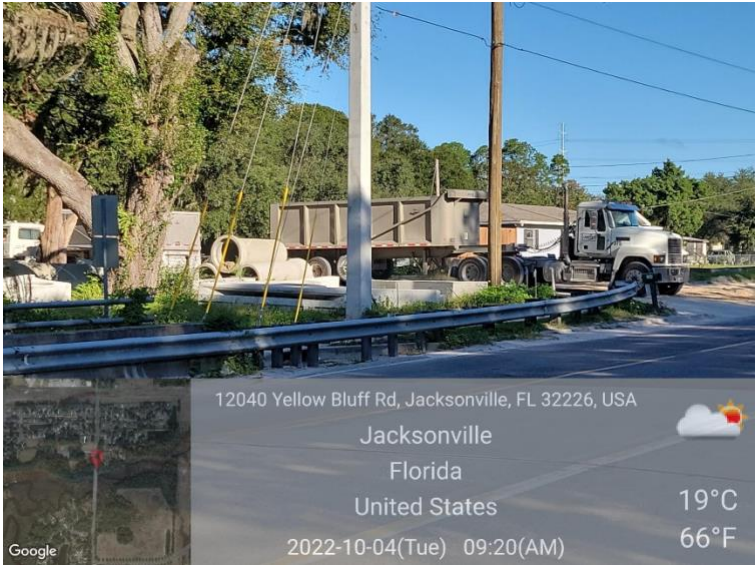

Limerock delivery at Pond 6

Limerock delivery at Pond 6

Eisman & Russo, Inc

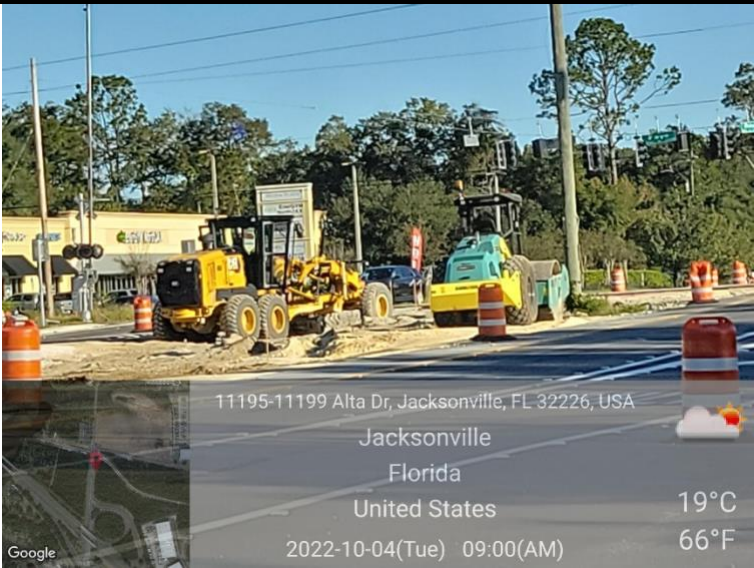

Sta 18+47 to 22+80 Demo median and place limerock in lieu of subgrade

Sta 18+47 to 22+80 Demo median



Stockpile new limerock at pond 6




Form and pour curb and sidewalk




Formed and poured Driveway curb and gutter



Formed and poured Driveway curb and gutter



Formed and poured Driveway curb and gutter



Formed and poured Driveway curb and gutter
