

## San Pablo Road (Beach Boulevard to Atlantic Boulevard)


### Project Phase

Construction – Phase 2A & 2B

### Upcoming Work

Work planned for next week –1-15-24 through 2-01-2. Work will progress along the entire corridor on the East side of the roadway. Once the East sidewalk and curbs are complete-Traffic will be shifted to facilitate construction of the west curb and sidewalk.

- JEA Work for watermain relocations (Nights)
- Storm drain crossing north of Beach Blvd. (Nights)
- Curb/Sidewalk Installation
- Lighting conduit installations
- Earthwork and grading for widening and new curb.
- Critical Wall Storm drain Tie-in at Drakes Pt.
- Earthwork for widening Ibis Point to Cocoanut Ln.
- Install Storm Drainage Ketch Cove to Atlantic.
- Install Storm Drainage Beach Blvd. to Castaway.

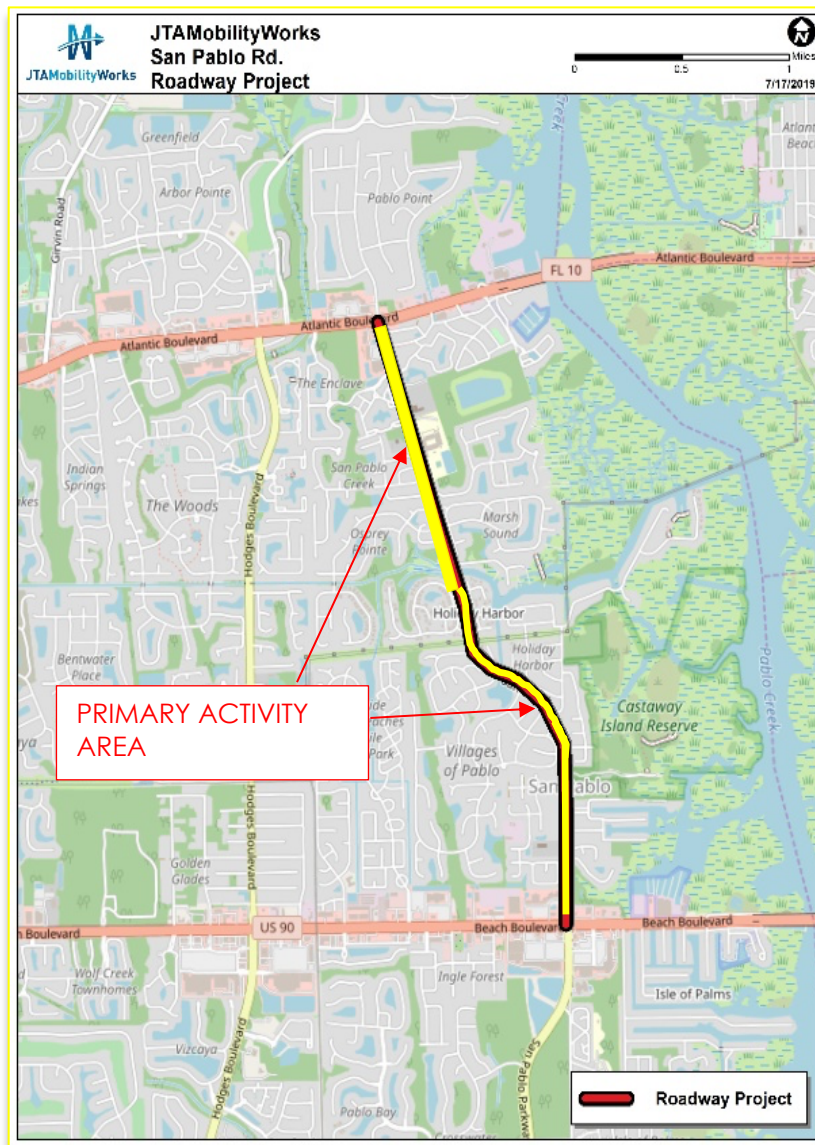

\*Note - Minor activities may be pursued in additional project areas
