

San Pablo Road (Beach Boulevard to Atlantic Boulevard)


Project Phase 2B/3A. SB traffic from Atlantic Blvd to Intracoastal Sound is anticipated to be shifted east to current median area on night of 7/19/24.

Construction – Phase 2B & 3A

Upcoming Work

Work planned for next week – 7-15-24 through 8-05-24

- Grading for new curb and turn lanes on west side.
- Storm drain structure installations on west side.
- Sod and pavement striping at night 7/17 to 7/19
- Continue construction of sidewalk on west side
- Asphalt paving daytime 7/10-7/17, 7/24&7/25, 7/28-8/2.
- Guardrail installations
- Pipe video and cleaning.
- Material removal at JEA Easement area.
- Curb installations on West side.
- Milling/removal of old asphalt 7/28 – 8/2

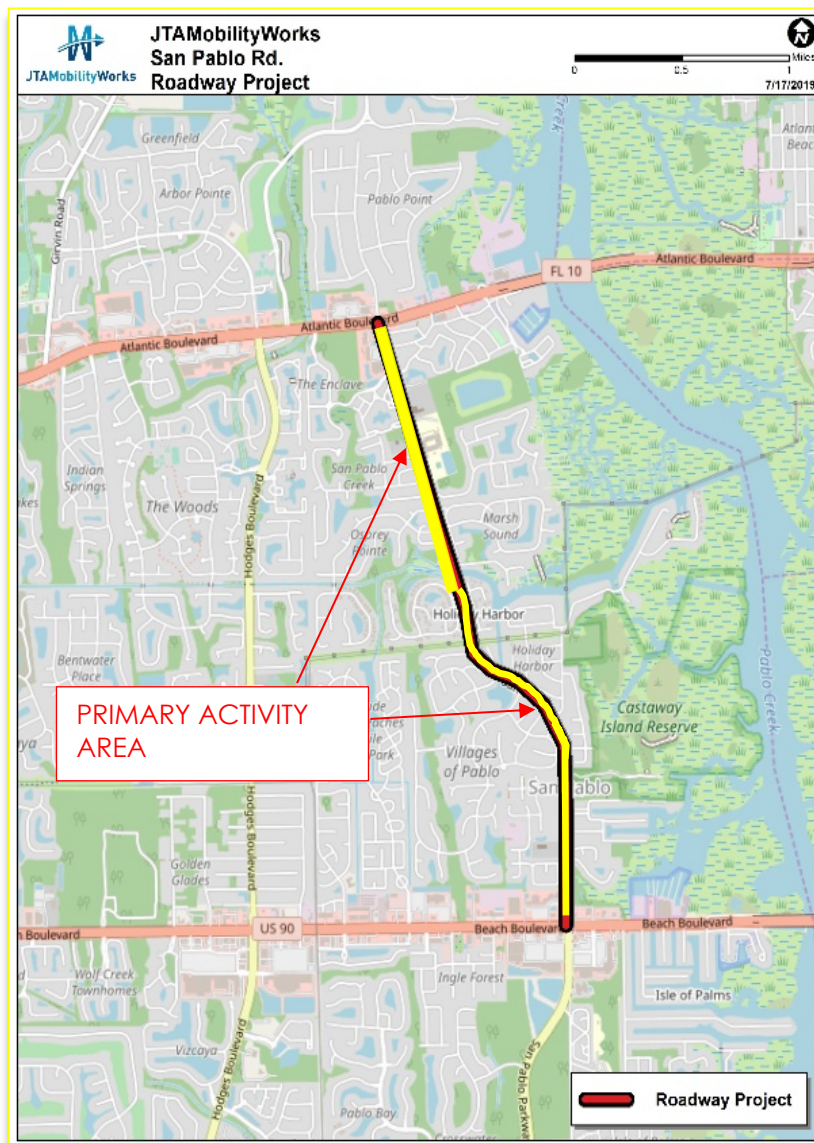

*Note - Minor activities may be pursued in additional project areas
