


# San Pablo Road (Beach Boulevard to Atlantic Boulevard)

**Project Phase** Construction – Phase 1B & 2A

## Upcoming Work

**Work planned for next week – 8-21-23 through 9-2-23**

- Ongoing AT&T Utility Work
- Storm Drainage Installation
- Signalization Bores to place conduit.
- Install low profile barrier wall on NB Lane
- Install Sheet Pile wall at Drakes Point
- Grading for curb and sidewalk on East side
- Abandoned watermain removal.

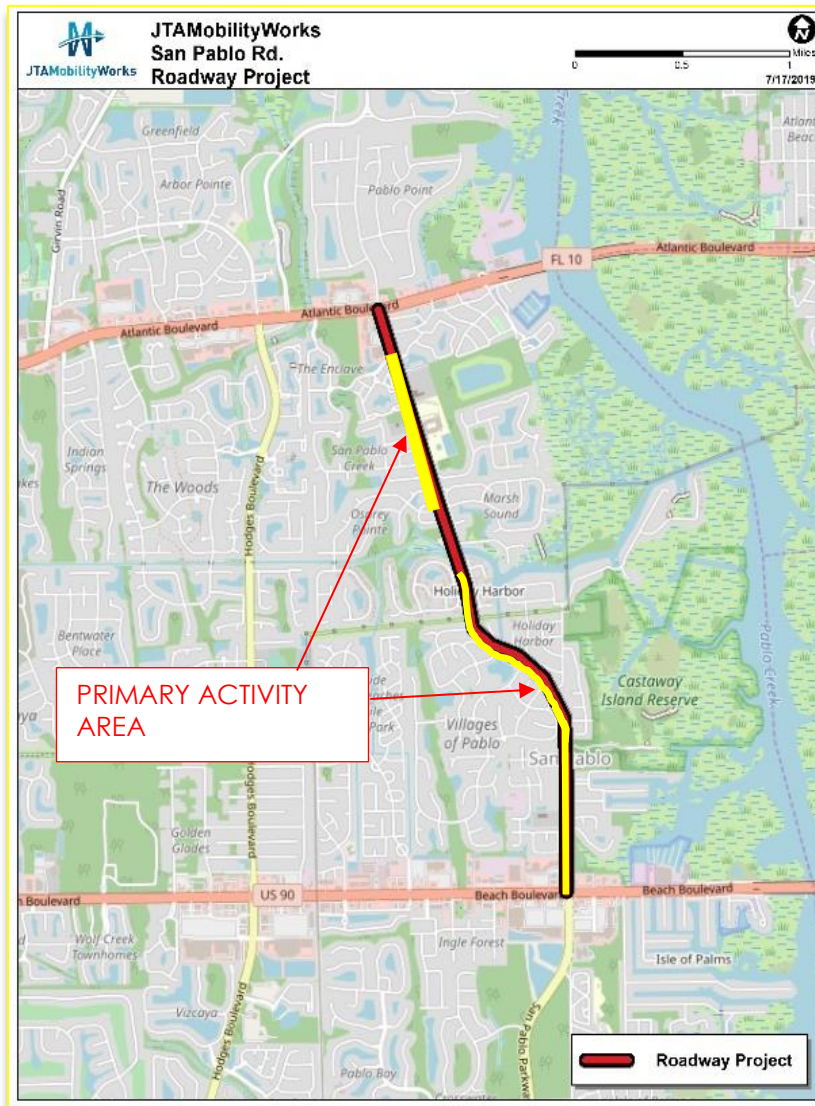

Traffic from Windjammer lane has been shifted onto temporary pavement for reconstruction of the old northbound lanes. Operations will consist of sheet pile wall construction at Drakes Point area and pipe work to install storm drainage in areas from Ketch Cove Dr. south to Beach Blvd along with excavation and grading to prep for construction of new curbs and sidewalk on East side of project. These daytime operations may require lane closures with flagging operations between the hours of 8AM and 4PM.

Beach Boulevard to

\*Note - Minor activities may be pursued in additional project areas
