

San Pablo Road (Beach Boulevard to Atlantic Boulevard)


Project Phase 2B/3A. NB traffic from Drakes Point to Atlantic Blvd. Has been shifted east to new pavement, SB traffic from Intracoastal sound to Drakes Point Dr. has also been shifted to the east.

Construction – Phase 2B & 3A

Upcoming Work

Work planned for next week – 6-17-24 through 7-08-24

- Grading for new curb and turn lanes on west side.
- Storm drain structure installations on west side.
- Continue construction of sidewalk and L-Walls
- Removal of temporary asphalt on west side.
- Removal of old sidewalks on west side.
- Relocation and installation of Pedestrian signals
- Sod placement
- Milling/removing medina area asphalt for replacement 7/1 to 7/6
- Asphalt paving median areas 7/08 to 7/19
- Pipe video and cleaning.

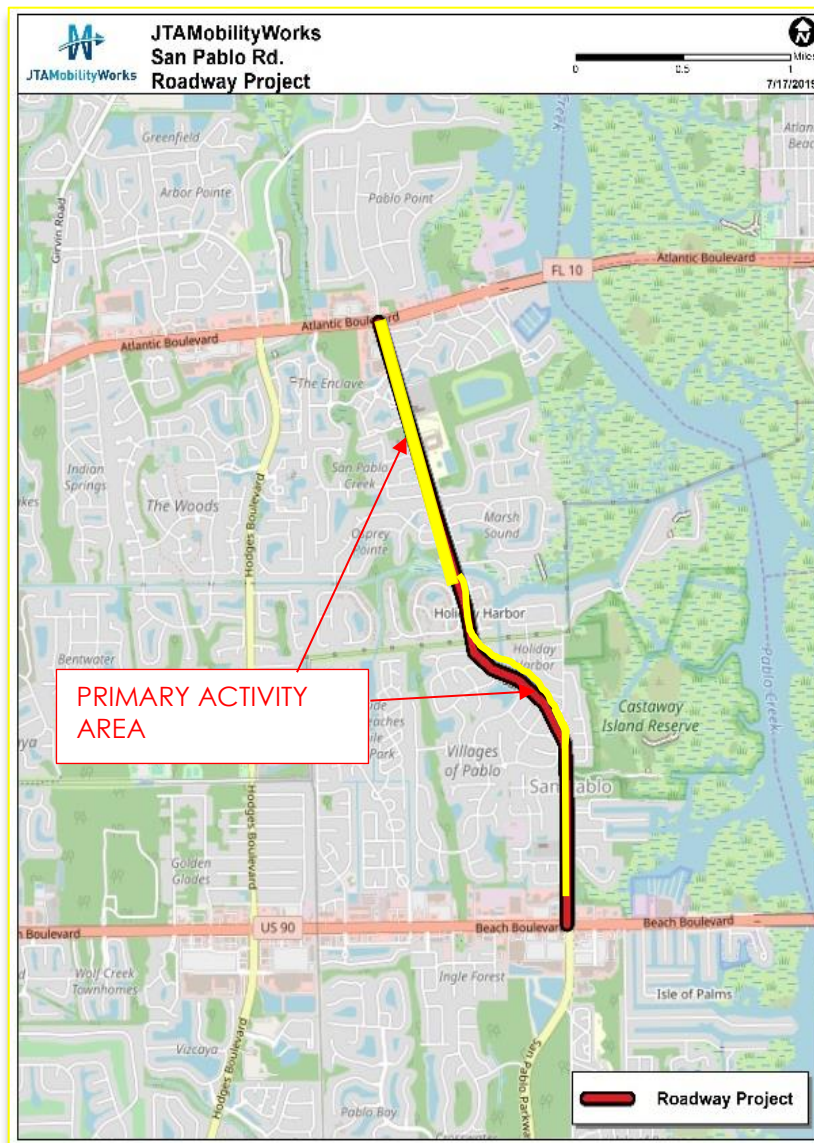

*Note - Minor pursued in additional project areas

activities may be
