

San Pablo Road (Beach Boulevard to Atlantic Boulevard)

Project Phase NB traffic has been shifted slightly Right onto new pavement from Drakes Point Dr south to Aqua Vista Dr. SB traffic in this same area will be shifted to the east on Friday night 4-19-24. Areas south of this location will be shifted to new pavement in the next 3-5 weeks.


Construction – Phase 2A & 3A

Upcoming Work

Work planned for next week - 4-8-24 through 4-28-24

- JEA pole removal
- Curb/Sidewalk Installation
- Mill existing asphalt in median south of Drakes Point Dr
- Asphalt and milling at Night work 4-11 to 4-16
- Grading for new turn lanes and widening
- Storm Drainage-complete final items on east side

- Construct sidewalk L-Walls
- Sidewalk L-Wall construction
- Striping for Traffic Switch
- Traffic Switch 4-19-24
- Remove sections of barrier wall-(Nights)

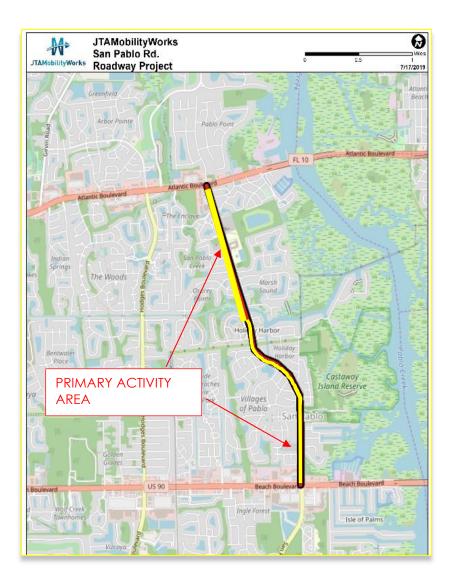

*Note - Minor activities may be pursued in additional project areas
